

District of Columbia Power Line Undergrounding (DC PLUG) Initiative – Feeder 00308

Presented to: ANC 3E

Presented by: Pepco and DDOT

September 12, 2019

www.dcpluginfo.com



Agenda

- Construction Schedule
- Scope of Work
- Construction Activities
- Project Notifications
- Community Outreach
- Contact Us

Construction Schedule

- Project Start: May 28, 2019
- Estimated Project Completion: May 1, 2020

- Normal Work Hours: 9:30 am to 3:30 pm (*working behind traffic drum*)
- Permitted Work Hours: 7:00 am to 7:00 pm (*working behind temporary pedestrian PVC barricade*)

- Contractors may work during the evening or on weekends with special after hours permit due to inclement weather delays.

Detailed Scope of Work


Civil Infrastructure Construction includes the following activities:

<ul style="list-style-type: none">• Removal and disposal of existing roadway pavement	<ul style="list-style-type: none">• Manhole construction
<ul style="list-style-type: none">• Removal and disposal of curb and gutter	<ul style="list-style-type: none">• Excavation and backfilling of all utility cuts
<ul style="list-style-type: none">• Removal and disposal of sidewalks and trees	<ul style="list-style-type: none">• Restore all utility cuts
<ul style="list-style-type: none">• Milling of existing asphalt pavement	<ul style="list-style-type: none">• Replace curb, gutter, and sidewalk
<ul style="list-style-type: none">• Installation of Pepco supplied materials	<ul style="list-style-type: none">• Replace topsoil, seed and mulch on all disturbed earth and grass.
<ul style="list-style-type: none">• Furnishing and installation of concrete for duct bank encasement	

Construction Activities - Two Week Look Ahead

Over the next two weeks, our contractor(s) will be working to install manholes, tapholes and transformer enclosures and laying conduit. This work will include trenching, backfilling and pouring concrete on the following blocks:


- 46th Street NW and Chesapeake Street NW (intersection)
- 49th and Brandywine Streets NW (intersection)
- Fessenden and 44th Streets NW (intersection)
- 46th and Davenport Streets NW (intersection)
- 4600 block of Chesapeake Street NW
- 4800 block of Chesapeake Street NW
- 4700 block of 46th Street NW.
- 5000 block of 44th Street NW

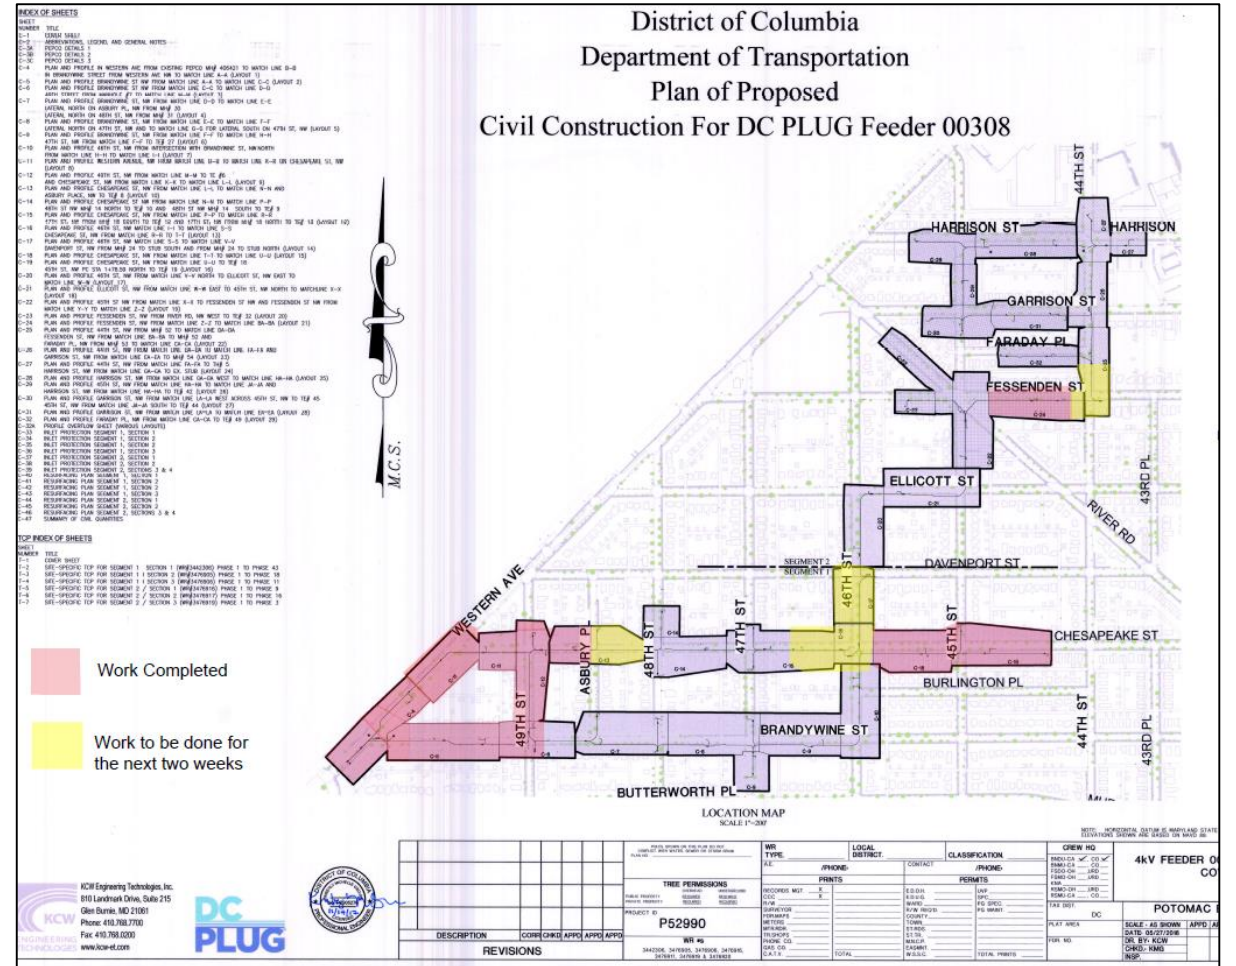

Projected 30-Day Construction Schedule

Over the 30-days, our contractor(s) will be working to install manholes, tapholes and transformer enclosures and laying conduit. This work will include trenching, backfilling and pouring concrete on the following blocks:

- 4800 block of Chesapeake St NW
- 4700 block of Asbury Pl NW
- 4700 block of Chesapeake St. NW
- 4600 block of 48th St NW
- 4709 46th St NW
- 4700 block of 46th St NW
- 46th & Davenport Sts NW (intersection)
- 4528 Davenport St NW
- 4601 Chesapeake St NW
- 46th & Chesapeake Sts NW (intersection)
- Brandywine St & Western Ave NW (intersection)
- 4645 Chesapeake St NW
- 48th & Chesapeake Sts NW (intersection)
- 4528 Davenport St NW
- 4355 Fessenden St NW
- 5000 block of 44th St NW
- 5007 44th St NW

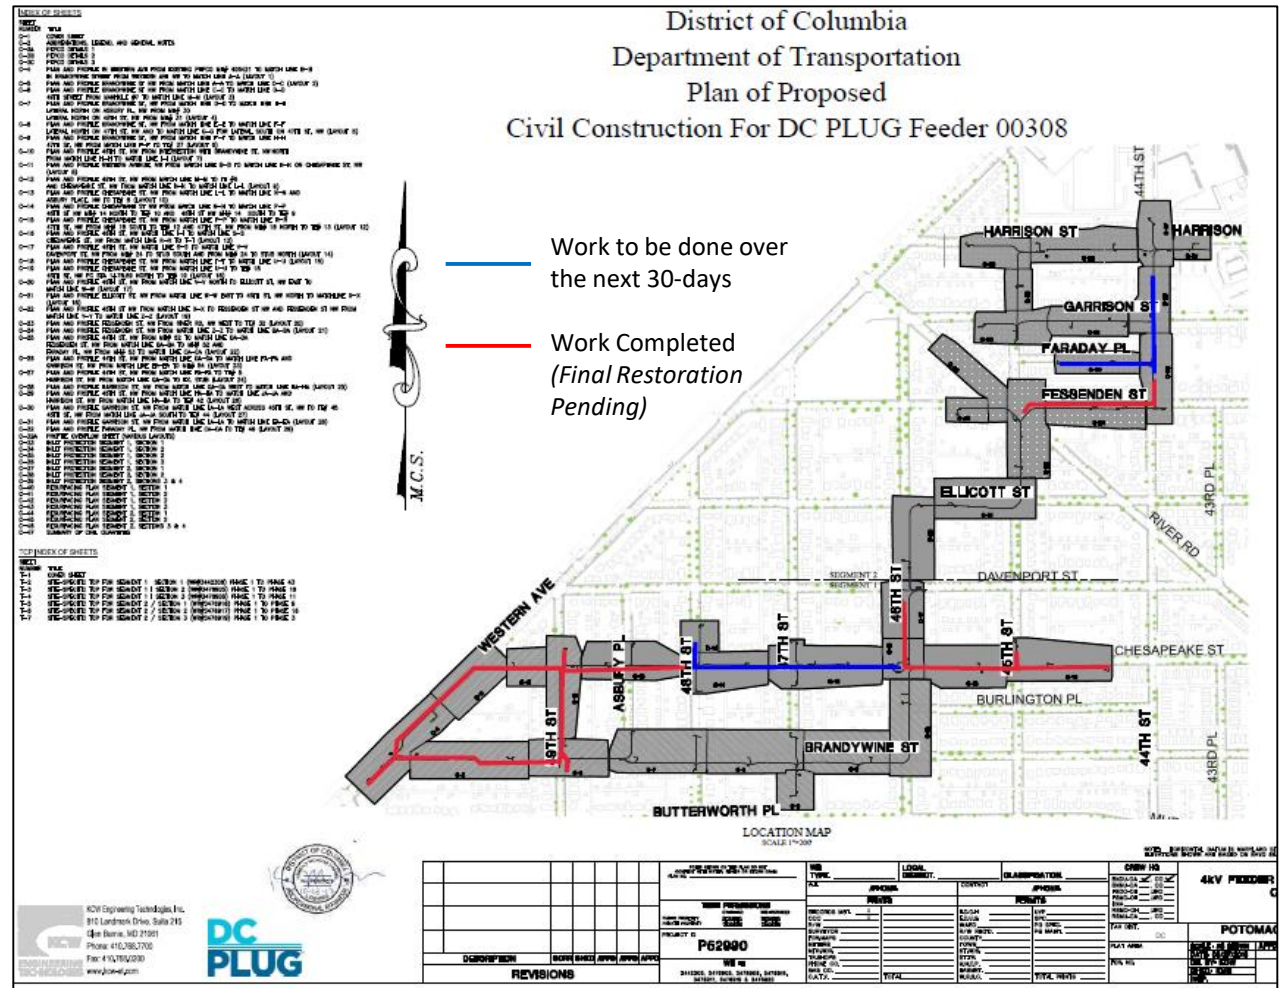

Project Notifications

- **15 Days Prior to Construction**
 - Impacted customers will receive a phone call of upcoming construction activity
- **7 Days Prior to Construction**
 - Impacted customers will receive a reminder doorhanger of upcoming construction activity
- **72 Hours Prior to Construction**
 - Emergency No Parking Signs will be posted on all impacted streets

Prior to the contractor mobilizing to your street, a layout of the proposed work area must be marked. Some of these work areas are by the curb and cannot be marked correctly due to parked vehicles. This is why signs are placed before the actual construction. Once the layout is complete, the contractor will begin mobilizing.



Community Outreach

- **In June 2019, the following outreach was performed:**
 - ANC 3E Project update (6/13)
 - Outbound calls to project impacted residents (6/20)
 - Saturday work notification distributions (6/20)
 - Saturday work notification distributions (6/26)
- **In July 2019, the following outreach was performed:**
 - Saturday work notification distributions (7/10)
 - ANC 3E Project update (7/11)
 - Saturday work notification distributions (7/24)
 - Saturday work notification distributions (7/31)

- **In August 2019, the following outreach was performed:**
 - Saturday work notification distributions (8/7)
 - Saturday work notification distributions (8/14)
 - Sent ANC 3E Commissioner Bender project update (8/22)
 - Overnight work notification distributions (8/30)
- **In September 2019, the following outreach was performed:**
 - Saturday work notification distributions (9/4)
 - Saturday work notification distributions (9/11)
 - ANC 3E project update (9/12)

Questions?



www.dcpluginfo.com



questions@dcpluginfo.com



1-844-758-4146



[@ddotdc](https://twitter.com/ddotdc) #DCPLUG
